



ID	Task Mode	Task Name	Duration	Start	Finish	Predec	Qtr 3, 2021			Qtr 4, 2021			Qtr 1, 2022			Qtr 2, 2022			Qtr 3, 2022			Qtr 4, 2022			Qtr 1, 2023
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
1		<b>Hickory Haven and Samary Forest Sanitary Sewer Project Preliminary Progress Schedule</b>	<b>330 days</b>																						
2		Notice to Proceed	1 day	Fri 8/27/21	Fri 8/27/21																				
3		Submittals	10 days	Mon 9/13/21	Fri 9/24/21																				
4		<b>Hickory Haven</b>	<b>115 days</b>	<b>Mon 9/27/21</b>	<b>Fri 3/4/22</b>																				
5		Constuction Flagging	10 days	Mon 9/27/21	Fri 10/8/21																				
6		Clearing & Grubbing	20 days	Mon 10/11/21	Fri 11/5/21	5																			
7		Construction Staking	5 days	Mon 11/8/21	Fri 11/12/21	6																			
8		Silt Fence and E&S	4 days	Mon 11/8/21	Thu 11/11/21	16																			
9		Pipe Order & Delivery	40 days	Mon 9/27/21	Fri 11/19/21	3																			
10		Install New 8" Sewer & Laterals in Easement from EX MH 1 to MH 5 = 1,206'	24 days	Mon 11/22/21	Thu 12/23/21	9																			
11		Install New 8" Sewer & Laterals on Holly Road from MH 3 to MH 8 = 415'	8 days	Fri 12/24/21	Tue 1/4/22	10																			
12		Install New 8" Sewer & Laterals on Birch Road & Cedar Circle from MH 7 to MH 10 = 486'	9 days	Wed 1/5/22	Mon 1/17/22	11																			
13		Install New 8" Sewer in Easement from EX MH 1 to MH 11 = 217'	4 days	Tue 1/18/22	Fri 1/21/22	12																			
14		Install New 8" Sewer & Laterals in Holly Lane from MH 11 to MH 15 = 313'	6 days	Mon 1/24/22	Mon 1/31/22	13																			
15		Install New 8" Sewer in Easement from MH 15 to MH 18 = 448'	9 days	Tue 2/1/22	Fri 2/11/22	14																			
16		Install New 8" Sewer & Laterals in Holly Lane from MH 11 to MH 13 = 258'	5 days	Mon 2/14/22	Fri 2/18/22	15																			
17		Install New 8" Sewer & Laterals in Easement from MH 12 to MH 14 = 257'	5 days	Mon 2/21/22	Fri 2/25/22	16																			
18		Install New 2" Force Main and Pressure Connections on Holly Lane = 306'	3 days	Mon 2/28/22	Wed 3/2/22	17																			
19		Permanent Restoration and Final E&S Work	2 days	Thu 3/3/22	Fri 3/4/22	18																			
20		<b>Samary Forest</b>	<b>111 days</b>	<b>Tue 2/1/22</b>	<b>Tue 7/5/22</b>																				
21		Constuction Flagging	5 days	Tue 2/1/22	Mon 2/7/22	14																			
22		Clearing & Grubbing	10 days	Tue 2/8/22	Mon 2/21/22	21																			
23		Construction Staking	10 days	Tue 2/22/22	Mon 3/7/22	22																			
24		Silt Fence and E&S	3 days	Tue 3/8/22	Thu 3/10/22	23																			
25		Install New 8" Sewer & Laterals in Easement from EX MH 246 to MH 41 = 1,428'	25 days	Fri 3/11/22	Thu 4/14/22	24																			
26		Install New 8" Sewer & Laterals in Easement from MH 41 to MH 47 = 1,293'	22 days	Fri 4/15/22	Mon 5/16/22	25																			
27		Install New 8" Sewer & Laterals in Easement & Henry Rd from MH 22 to MH 26 = 1,275'	22 days	Tue 5/17/22	Wed 6/15/22	26																			

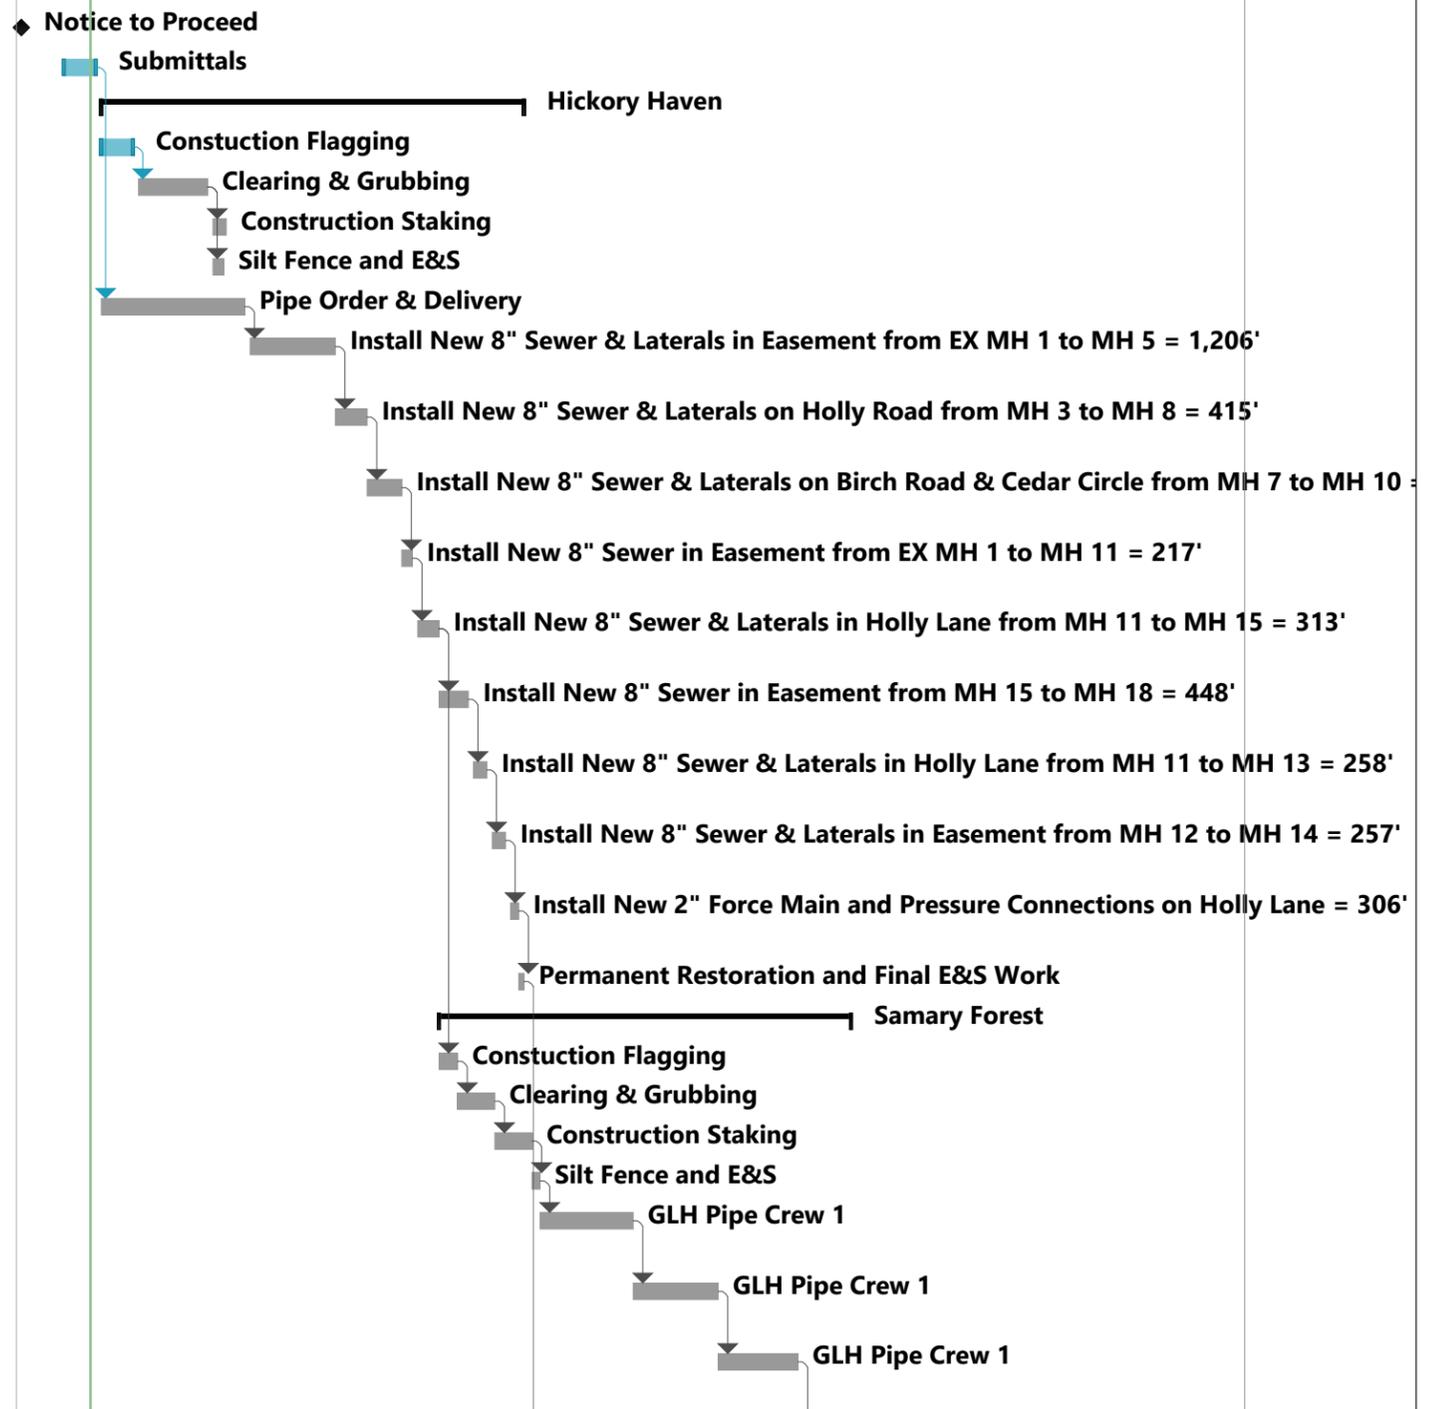

Project: Hickory Haven and Samary Forest Date: Thu 9/23/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predec	Qtr 3, 2021			Qtr 4, 2021			Qtr 1, 2022			Qtr 2, 2022			Qtr 3, 2022			Qtr 4, 2022			Qtr 1, 2023
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
28		Install New 8" Sewer & Laterals in Henry Rd from MH 26 to MH 28 = 444'	8 days	Thu 6/16/22	Mon 6/27/22	27																			
29		Install New 8" Sewer & Laterals in Whippoorwill Rd from MH 28 to MH 30 = 228'	4 days	Tue 6/28/22	Fri 7/1/22	28																			
30		Permanent Restoration	2 days	Mon 7/4/22	Tue 7/5/22	29																			
31		Asphalt Restoration of Hickory Haven	4 days	Mon 3/7/22	Thu 3/10/22	19																			
32		Asphalt Restoration of Samary Forest	4 days	Wed 7/6/22	Mon 7/11/22	30																			
33		Substantial Completion	1 day	Sat 7/23/22	Sat 7/23/22																				
34		Punchlist Items	21 days	Mon 7/25/22	Mon 8/22/22	33																			
35		Final Completion	1 day	Mon 8/22/22	Mon 8/22/22																				

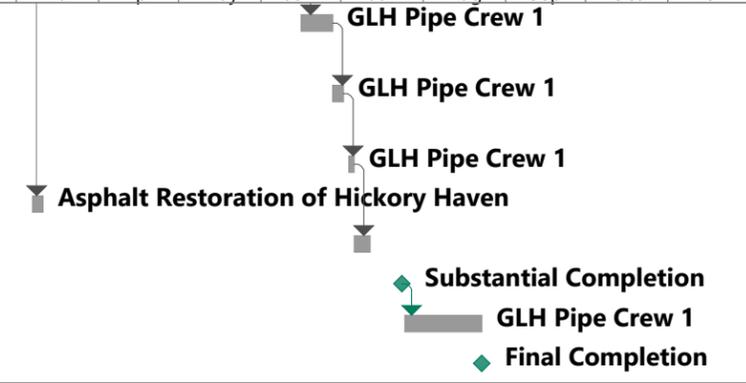

Project: Hickory Haven and Samary Forest Date: Thu 9/23/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
